KTest

更に上のクオリティ　更に上のサービス

問題集

Exam : **PK0-005**

Title : CompTIA
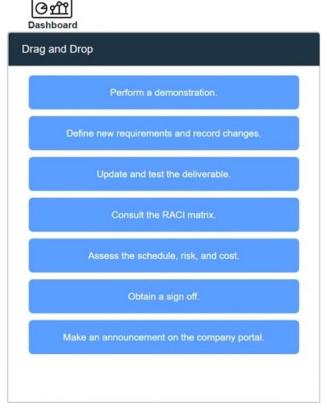Project+Certification

Version : DEMO

1.DRAG DROP -

During a gate review meeting, the deliverable was rejected by the customer.

Review the dashboard.

Part 1: Drag and drop each task, placing them in the correct order based on the project change control process.

Part 2: Select the proper document(s) to be updated.

Part 1   Part 2

Dashboard

Change Control Process

1	?
2	?
3	?
4	?
5	Select the appropriate document(s) to update.
6	?
7	?
8	?

Drag and Drop

Perform a demonstration.

Define new requirements and record changes.

Update and test the deliverable.

Consult the RACI matrix.

Assess the schedule, risk, and cost.

Obtain a sign off.

Make an announcement on the company portal.

Part 1   Part 2

Dashboard

Change Control Process

1	?
2	?
3	?
4	?
5	Select the appropriate document(s) to update.
6	?
7	?
8	?

Question Options

Select the appropriate document(s) to update.

- Risk register
- Schedule
- Statement of work
- Organizational chart
- Change log
- Issues log
- WBS dictionary

Answer:

Part 1   Part 2

Dashboard

Change Control Process

1	Define new requirements and record changes.
2	Assess the schedule, risk, and cost.
3	Update and test the deliverable.
4	Perform a demonstration.
5	Select the appropriate document(s) to update.
6	?
7	?
8	?

Drag and Drop

- Perform a demonstration.
- Define new requirements and record changes.
- Update and test the deliverable.
- Consult the RACI matrix.
- Assess the schedule, risk, and cost.
- Obtain a sign off.
- Make an announcement on the company portal.

Part 1   Part 2

Dashboard

Change Control Process

1	?
2	?
3	?
4	?
5	Select the appropriate document(s) to update.
6	Statement of work
7	Schedule
8	Change log

Question Options

Select the appropriate document(s) to update.

- Risk register
- Schedule
- Statement of work
- Organizational chart
- Change log
- Issues log
- WBS dictionary

2.A PM is responsible for implementing a new customer relationship management system and has learned that the sales organization is reluctant to utilize the new system. The organization's reluctance could jeopardize the success of the project.

Which of the following steps should be taken to understand the adoption issues and gain organizational acceptance of the initiative? (Choose two.)

A. Train users on the proper use of the system.

B. Escalate the issue to the CCB.

C. Hold sessions to understand user challenges.

D. Track system usage and report user activity.

E. Log the issue in the project risk register.

F. Create a memorandum of acceptable use.

Answer: CE

3.Following a successful release, a project manager sent a survey to all stakeholders to gain an understanding of opportunity areas for the team.

Which of the following can use the survey results as an input?

A. Daily stand-up

B. Project momentum

C. Performance feedback

D. Meeting minutes

Answer: C

4.Which of the following is an activity that should be used in the closing phase of a project to support the project triple constraint?

A. Evaluating the project
B. Releasing the resources
C. Closing the contracts
D. Reconciling the budget
Answer: D

5.During a quality analysis review, the causes of several issues have been highlighted.
Which of the following should the project manager use to identify the MOST important causes?
A. Ishikawa diagram
B. Scatter diagram
C. Pareto chart
D. Decision tree
Answer: C
